

icc



www.iccproject.com

Anacostia Watershed


Status of Highway Construction

ES/CM Construction

ES/CM Schedule

18 Feb 2010

Construction Status

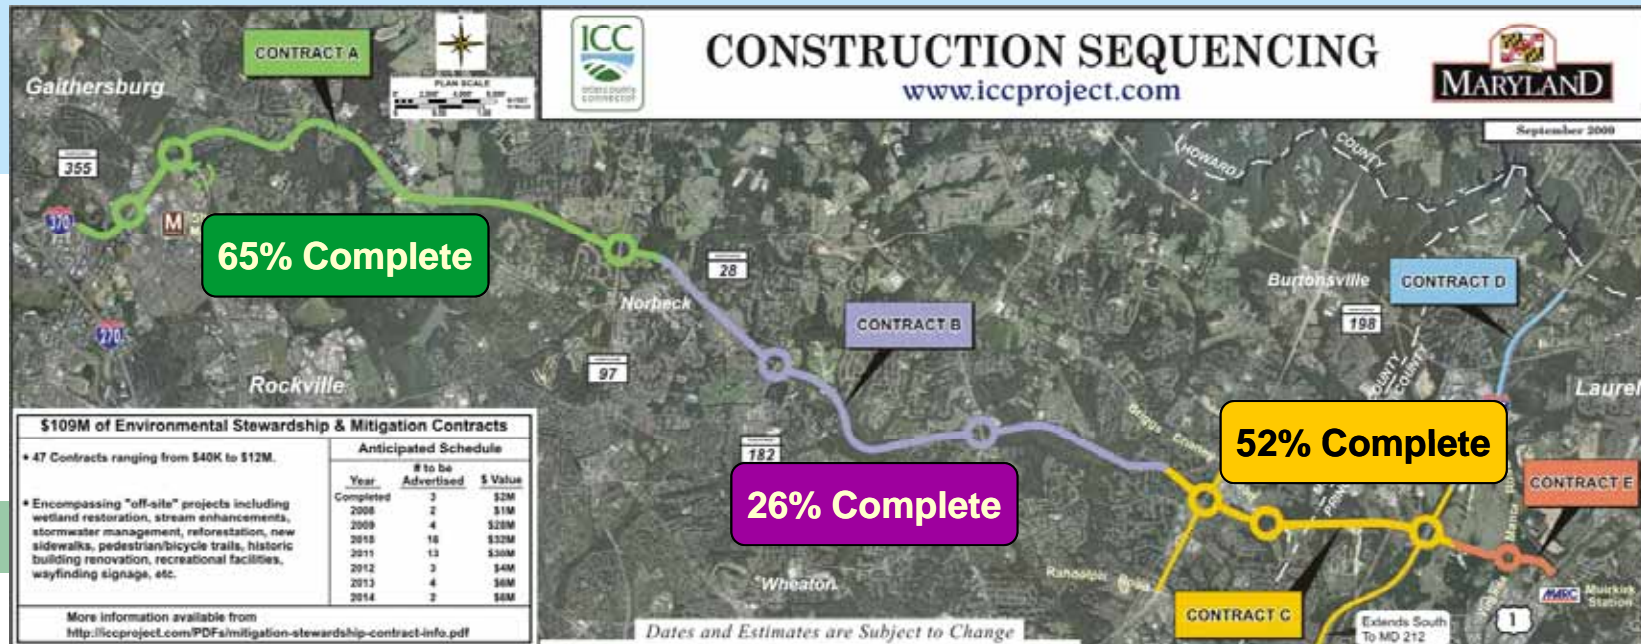

\$109M of Environmental Stewardship & Mitigation Contracts

- 47 Contracts ranging from \$40K to \$12M.
- Encompassing "off-site" projects including wetland restoration, stream enhancements, stormwater management, reforestation, new sidewalks, pedestrian/bicycle trails, historic building renovation, recreational facilities, wayfinding signage, etc.

More information available from <http://iccproject.com/PDFs/mitigation-stewardship-contract-info.pdf>

Anticipated Schedule		
Year	# to be Advertised	\$ Value
Completed	3	\$2M
2008	2	\$1M
2009	4	\$28M
2010	16	\$32M
2011	13	\$38M
2012	3	\$4M
2013	4	\$8M
2014	2	\$8M


Contract A I-270 / I-370 to MD 97 Contract # AT3765960	Contract B MD 97 to US 29 Contract # AT3765B60	Contract C US 29 to I-95 Contract # AT3765C60	Contract D Collector-Distributor Roads Along I-95 Contract # AT3765D60	Contract E I-95 to US 1 Contract # AT3765E60
\$478.7M (Contract Amount)	\$559.7M (Contract Amount)	\$513.9M (Contract Amount)	\$70M to \$85M (Year of Expenditure \$)	\$50M to \$65M (Year of Expenditure \$)
NTP: 11.13.2007 Open: Fall 2010	NTP: 1.16.2009 Open: Late 2011	NTP: 4.7.2008 Open: Late 2011	Deferred	NTP: TBD Open: TBD
7.2 Mainline Miles	7.0 Mainline Miles	3.7 Mainline Miles 2.5 Miles Along I-95 2.0 Miles Along US 29	3.0 Collector-Distributor Miles 4.9 Miles of I-95 Resurfacing	0.9 Mainline Miles 0.7 Miles Along US 1
3 Interchanges	2 Interchanges	3 Interchanges		1 Interchange 1 Intersection
D-B Team: Intercounty Constructors (IC) Rockville, Maryland	D-B Team: MD 200 Constructors Beltsville, Maryland	D-B Team: ICC Constructors (IC3) Beltsville, Maryland	110,000 SY Paving 315,000 SY Milling & Resurfacing 1.10M CY Cut 1 New Single Bridge	80,000 SY Paving 0.35M CY Cut 1 New Dual Bridge
A JV of: Granite, Corman and Wagman	A JV of: Kiewit, Corman and Wagman	A JV of: Shirley, Clark, Atkinson, Facchina & Trumbull		

	Governor: Martin O'Malley Lt. Governor: Anthony G. Brown	MDOT Secretary: Beverley K. Swaim-Staley Deputy Secretary: Harold M. Bartlett	MdTA Exec. Secretary: Ronald L. Freeland SHA Administrator: Neil J. Pedersen
--	---	--	---

Construction Status

Contract B – Bridge 28 ov NW Branch

Setting Girders



Construction Status

Contract B – Temp Bridge 33/Good Hope



Minimized clearing for access

Construction Status Contract B near Colesville Depot



ESC Berm along Stone access road

Construction Upcoming

Contract B – MD97 to US29

Construction of Bridges over NW Branch

Installation of E&S Controls and access road in Paint Branch

Construction of Structures in Paint Branch

Construction Schedule

Contract C – US29 to I-95

Construction of Bridge over Little Paint Branch

US29 and I-95 Interchanges

Construction of culvert carrying 6J (trib to Indian Creek)

Sediment Control - New Technology


Wheel Washing



Sediment Control - New Technology Wheel Washing



ICC ES/CM/CS Sites

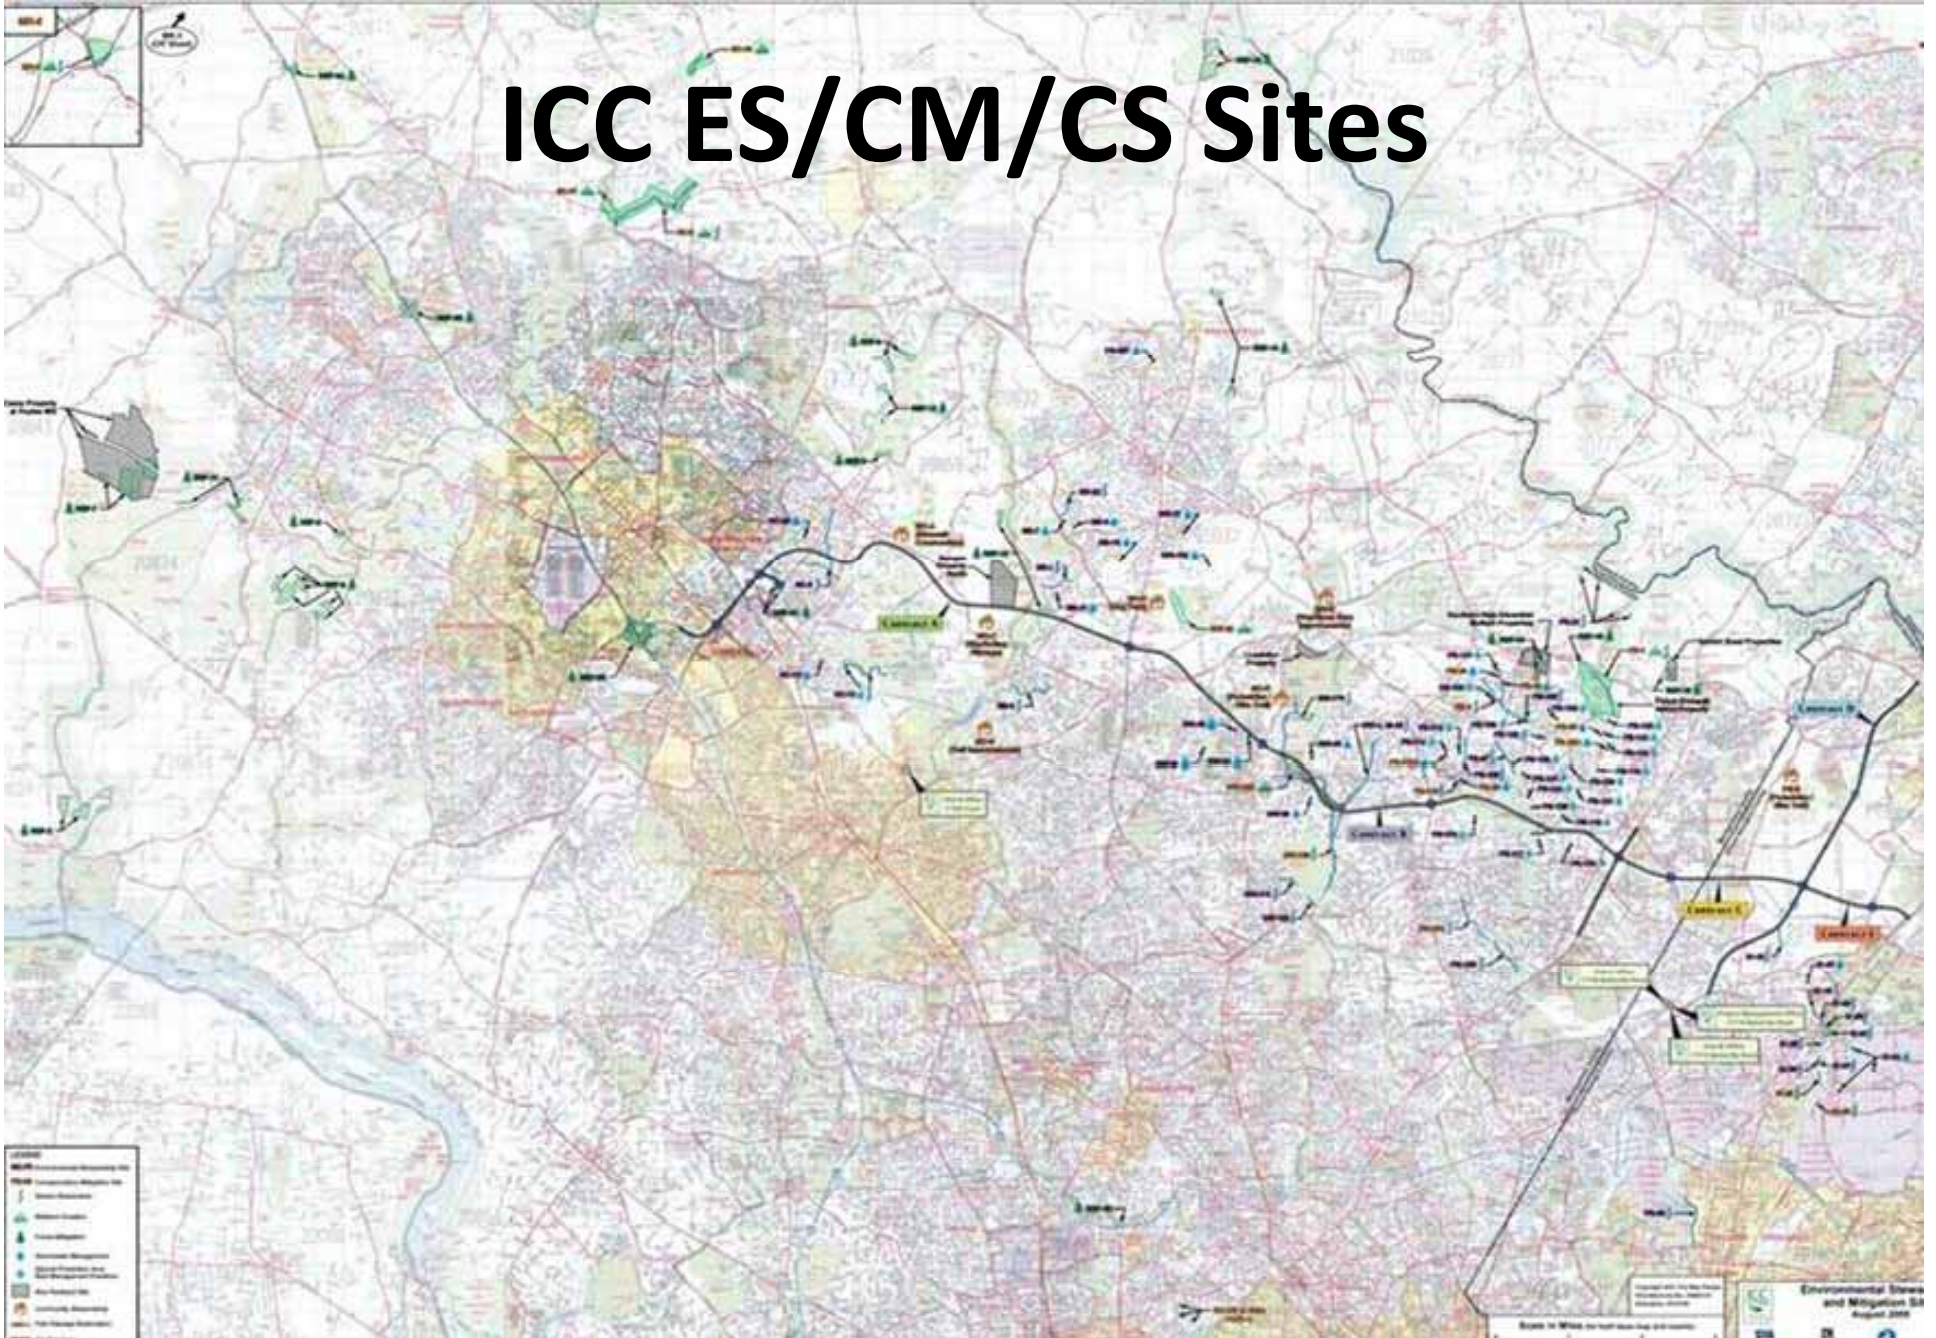

Information Updates Upcoming

iccproject.com


Live map showing Stewardship and Mitigation Projects

'Roll Over' to get basic info on project

'Click On' to get detailed info on project

'Address Locator'

WQ data to be added




Robert E. Shreeve
Environmental Manager
Office of the Intercounty Connector
State Highway Administration



410/545-8644

RShreeve@sha.state.md.us

www.iccproject.com





Sediment Basin E-7

Temp. Swale
E108-T4

Rain-for Rent
System (enlarge
the photo to see
pump lines)

Outfall of Storm
Drain into Indian
Creek





SB E-7 under construction

TS E106-T1

Additional Sediment Trap added as Field Change

Sediment Trap
SOST E128-T1

